



New Construction

PROGRESS UPDATE

February 2023

Southeast Pre K-12 School



PROJECT SUMMARY

Site Development & Landscaping

February 2023 Progress

- Site
- Utilities
 - Continue Site Lighting Conduit– 75%
 - Underground Power Conduit– 75%
 - Underground Data Conduit– 90%
 - Light Pole Bases Installation– 80%
 - Water Line Installation– 30%

Upcoming Progress

- Continue Installing Water Line




PROJECT SUMMARY

Area A


February 2023 Progress

- Under Slab Branch Conduit – 100%
- Pour Slab on Grade– 100%
- CMU Walls to Bearing– 80%

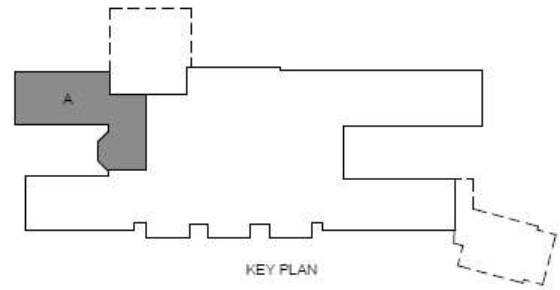

Upcoming Progress

- Setting Steel Lintels and Precast Planks

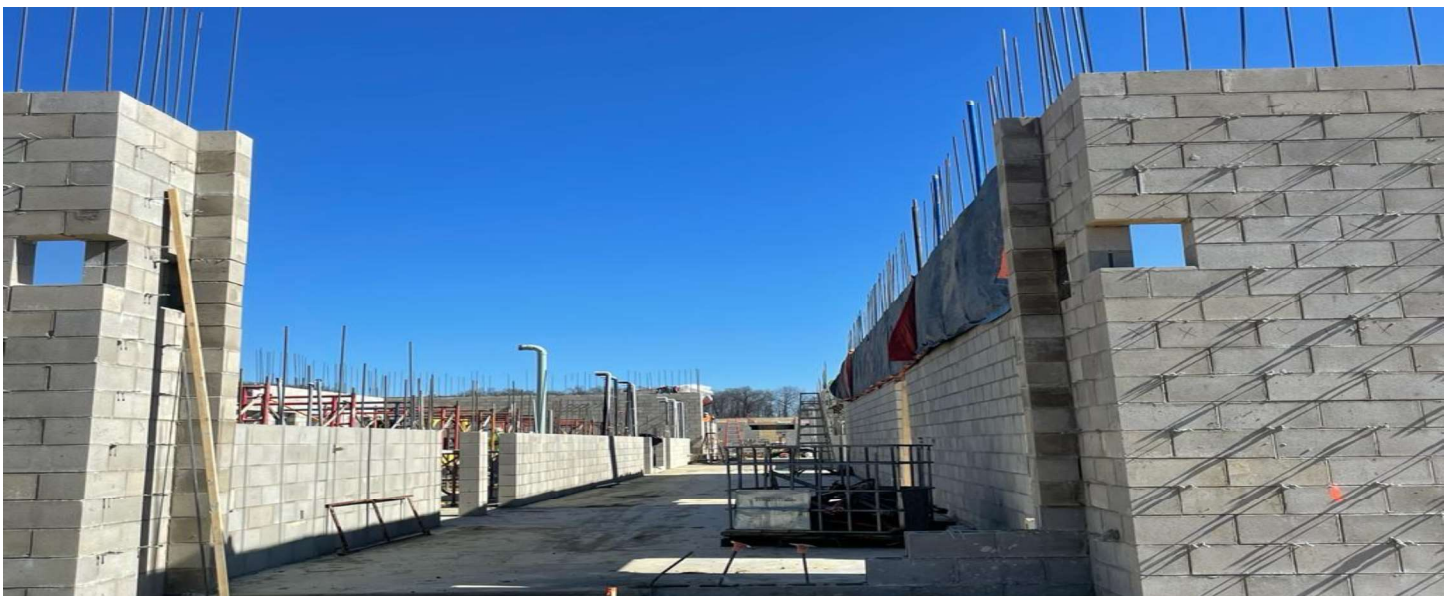


PROJECT SUMMARY

Area B

February 2023 Progress

- Foundations– 85%
- Underground Electrical Mains– 100%
- Below Grade CMU– 30%

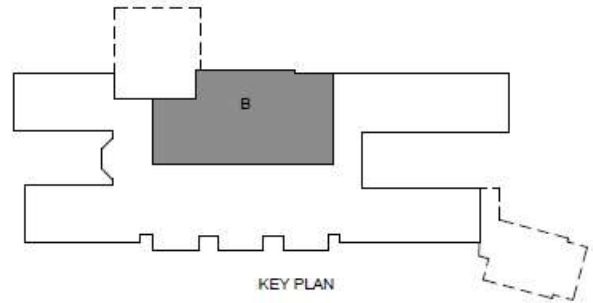

Upcoming Progress

- Continuing Foundations and Underground Electrical Mains.
- Continue Below Grade CMU




PROJECT SUMMARY

Area C

February 2023 Progress

- Pour Slab on Grade– 50%
- CMU Walls to Bearing– 100%
- Set Precast Planks– 100%

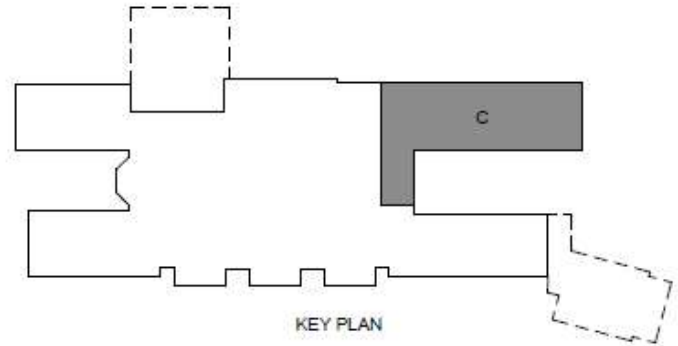

Upcoming Progress

- Complete Pouring Slab on Grade
- Grouting Precast Planks




PROJECT SUMMARY

Area D


February 2023 Progress

- Pour Slab on Grade— 100%
- Plumbing Carriers Ongoing— 50%

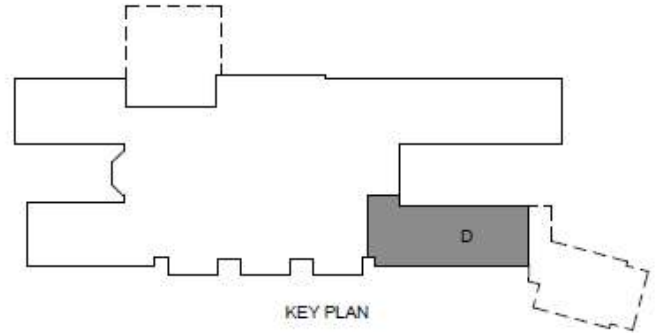

Upcoming Progress

- Continue Plumbing Carriers

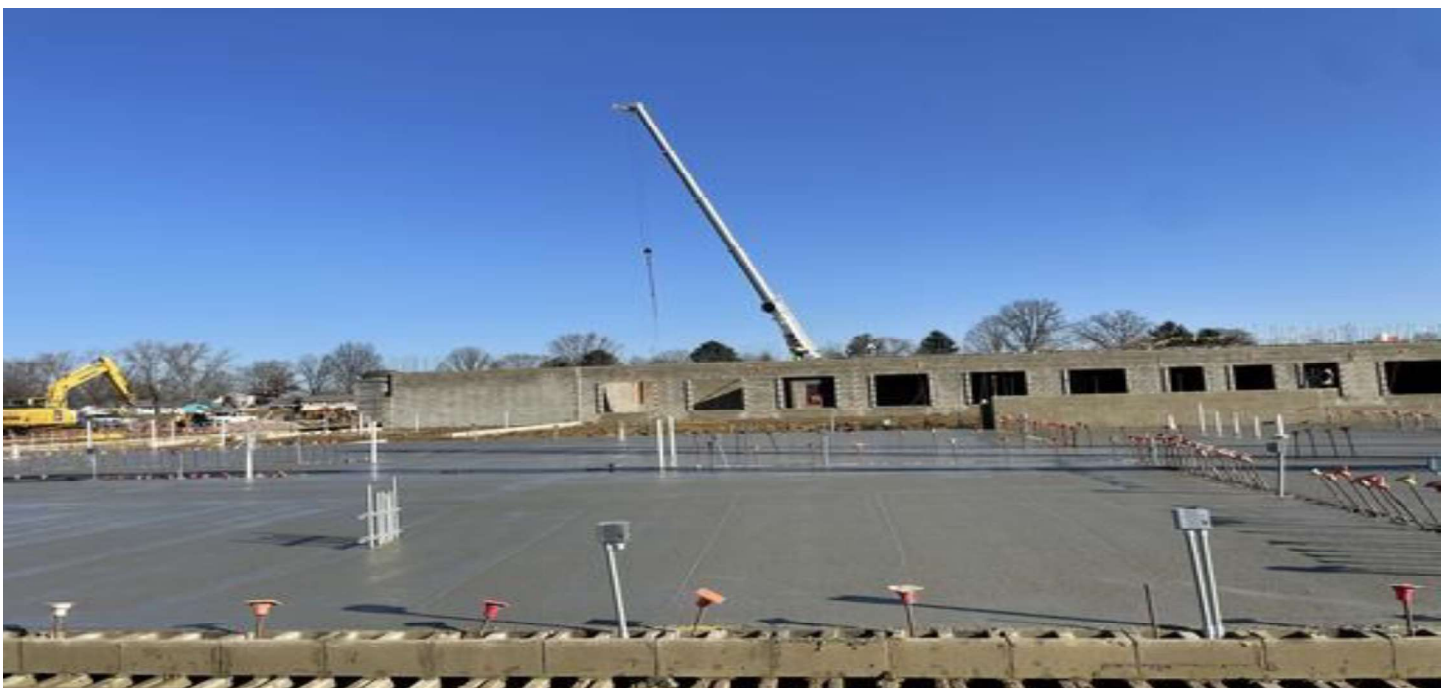

PROJECT SUMMARY


Area E

February 2023 Progress

- Underground Sanitary– 100%
- CMU to Bearing– 5%
- Pour Slab on Grade Locker Room– 100%

Upcoming Progress

- Continue CMU to Bearing
(weather permitting)

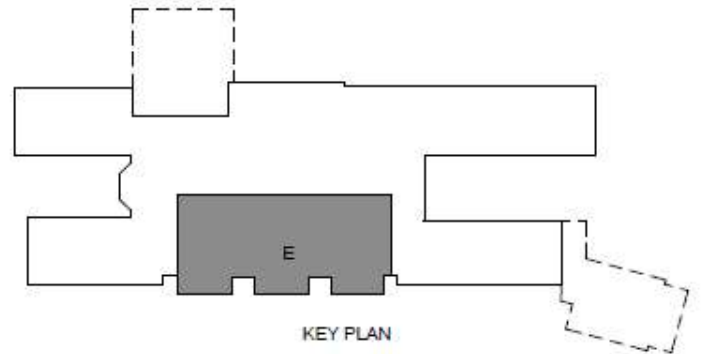


PROJECT SUMMARY

Area F

February 2023 Progress

- Slab on Grade Preparation– 100%
- Electric Branch Conduit– 100%

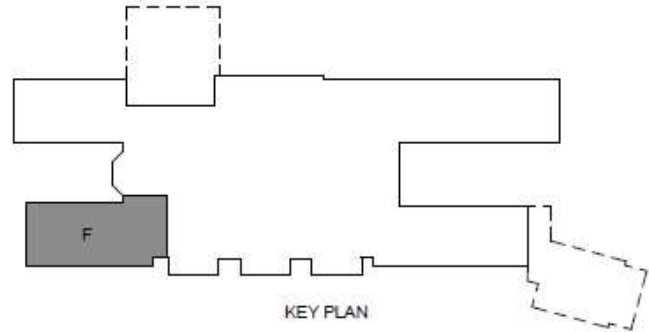

Upcoming Progress

- Pouring Slab on Grade
(Weather Permitting)






PROJECT SUMMARY

Area G

February 2023 Progress

- Below Grade CMU– 100%
- Prepare Slab on Grade– 40%

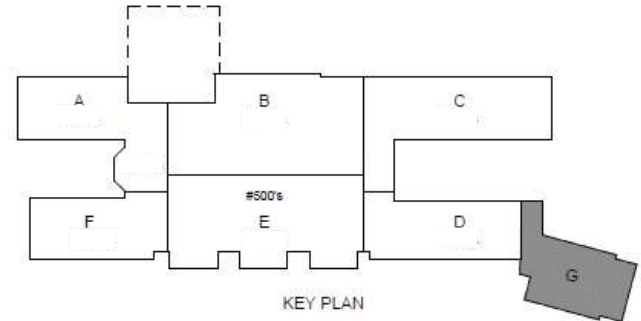

Upcoming Progress

- Continue Preparing Slab on Grade

